




DHS/DCT Agency Transitions

Daniel R. Storkamp | Operations Services Executive Director

A useful metaphor

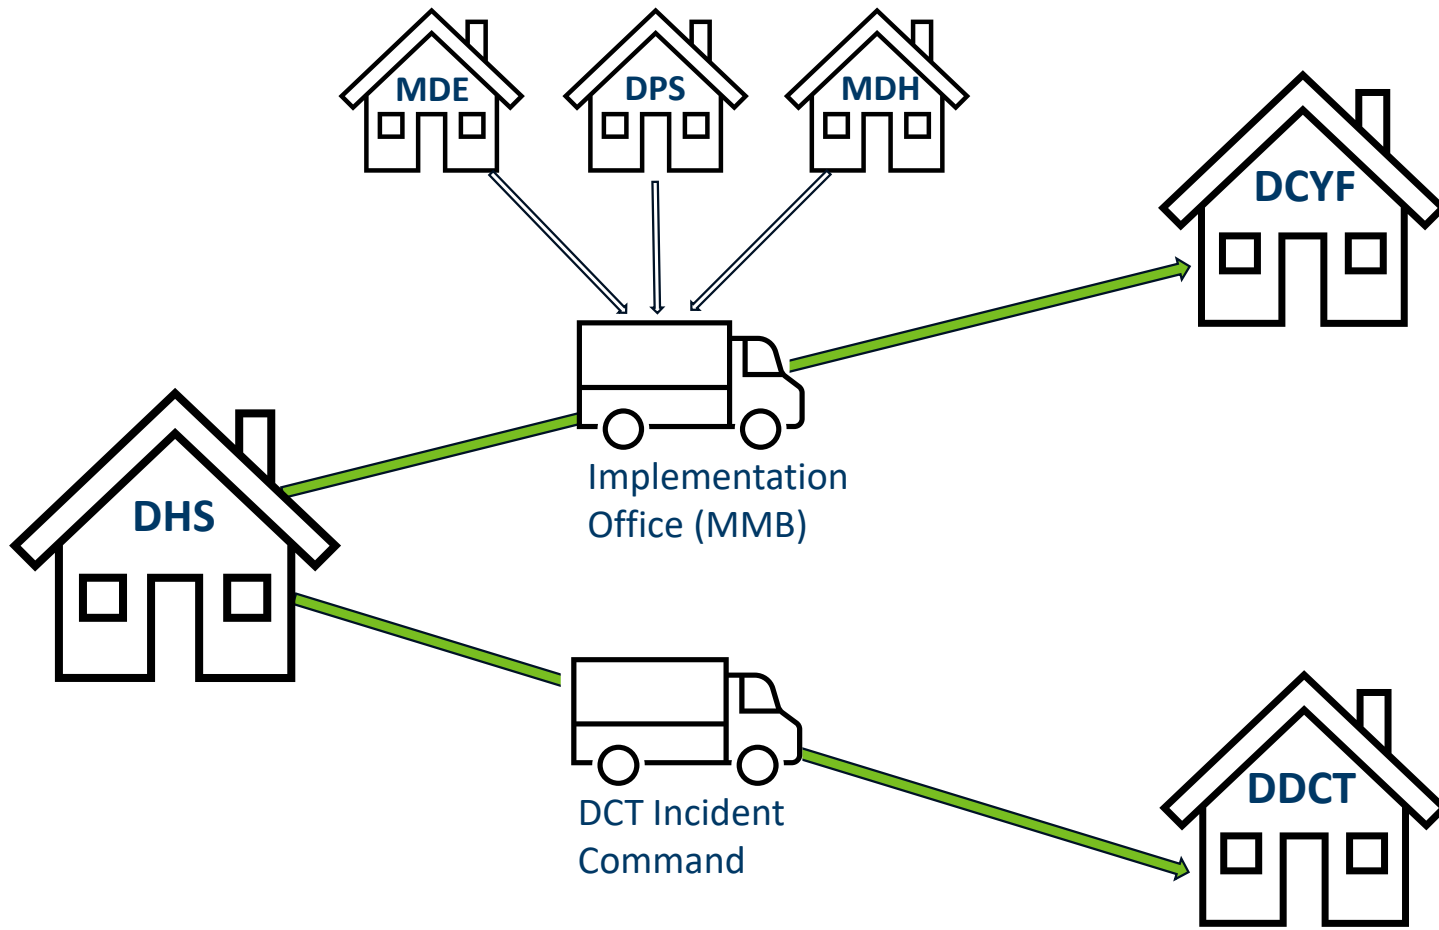

Joint timeline

Legislative Session

1/1/2025
DCT Created

7/1/2025
New DCT
Creation Date
Being
Discussed

Q3
2023

Q4
2023

Q1
2024

Q2
2024

Q3
2024

Q4
2024

Q1
2025

Q2
2025

7/1/23


DCYF
Implementation
Office Est.

7/1/24


DCYF Created/
Commissioner
appointed

Core programs transfer to DCYF


Incident command team

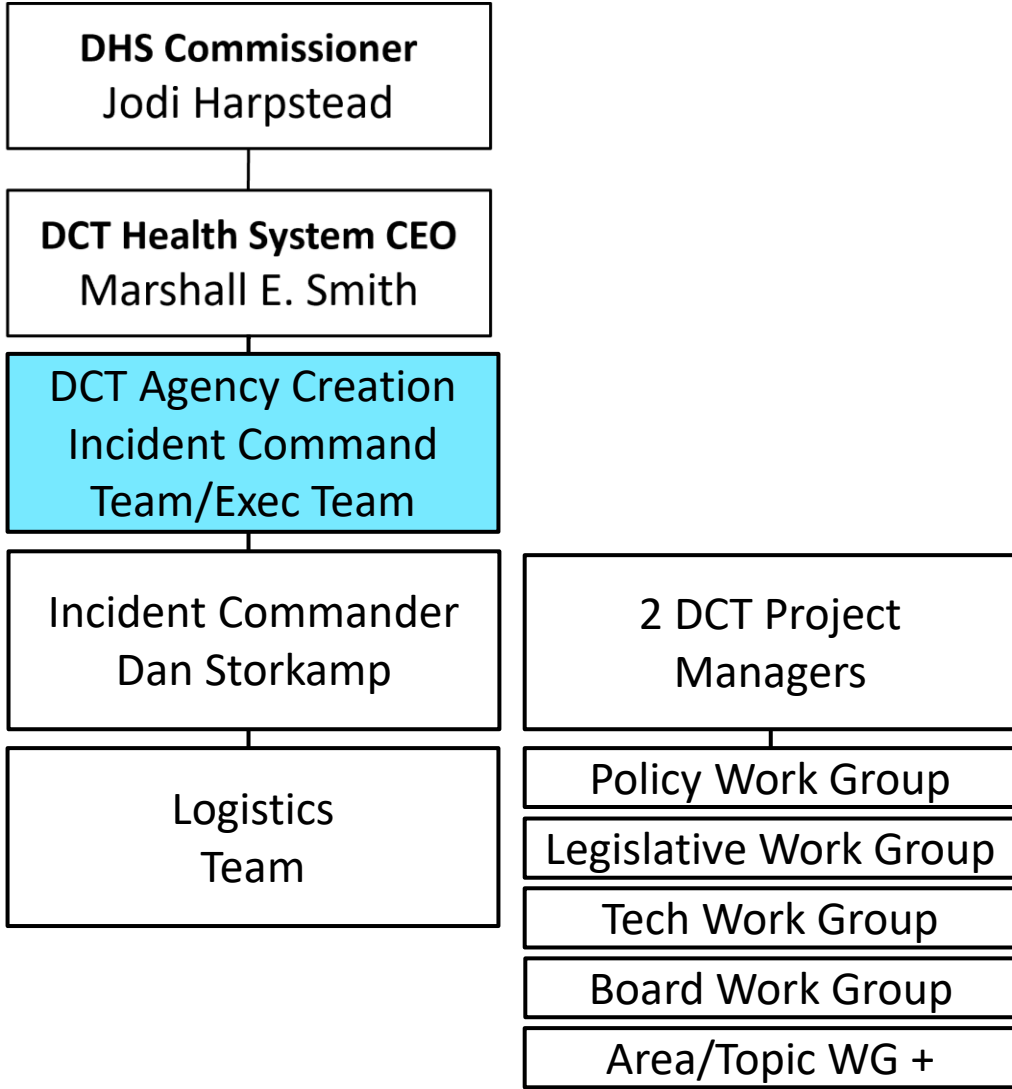

DCT transition legislative language

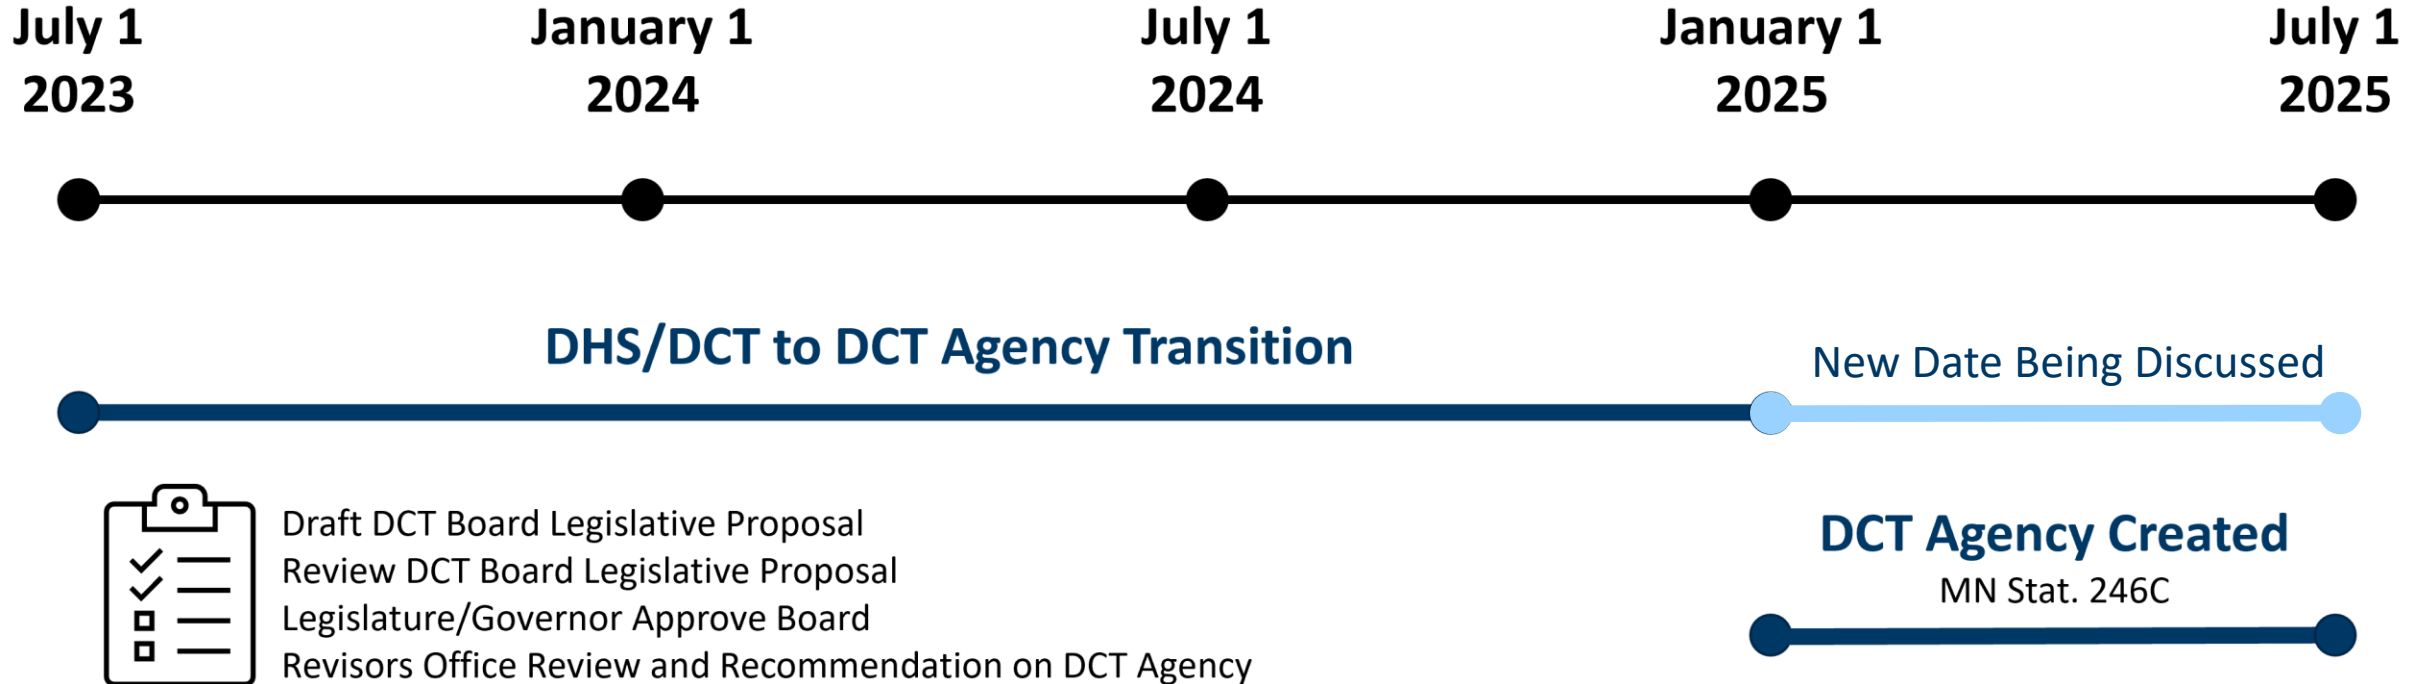

DCT transition priority

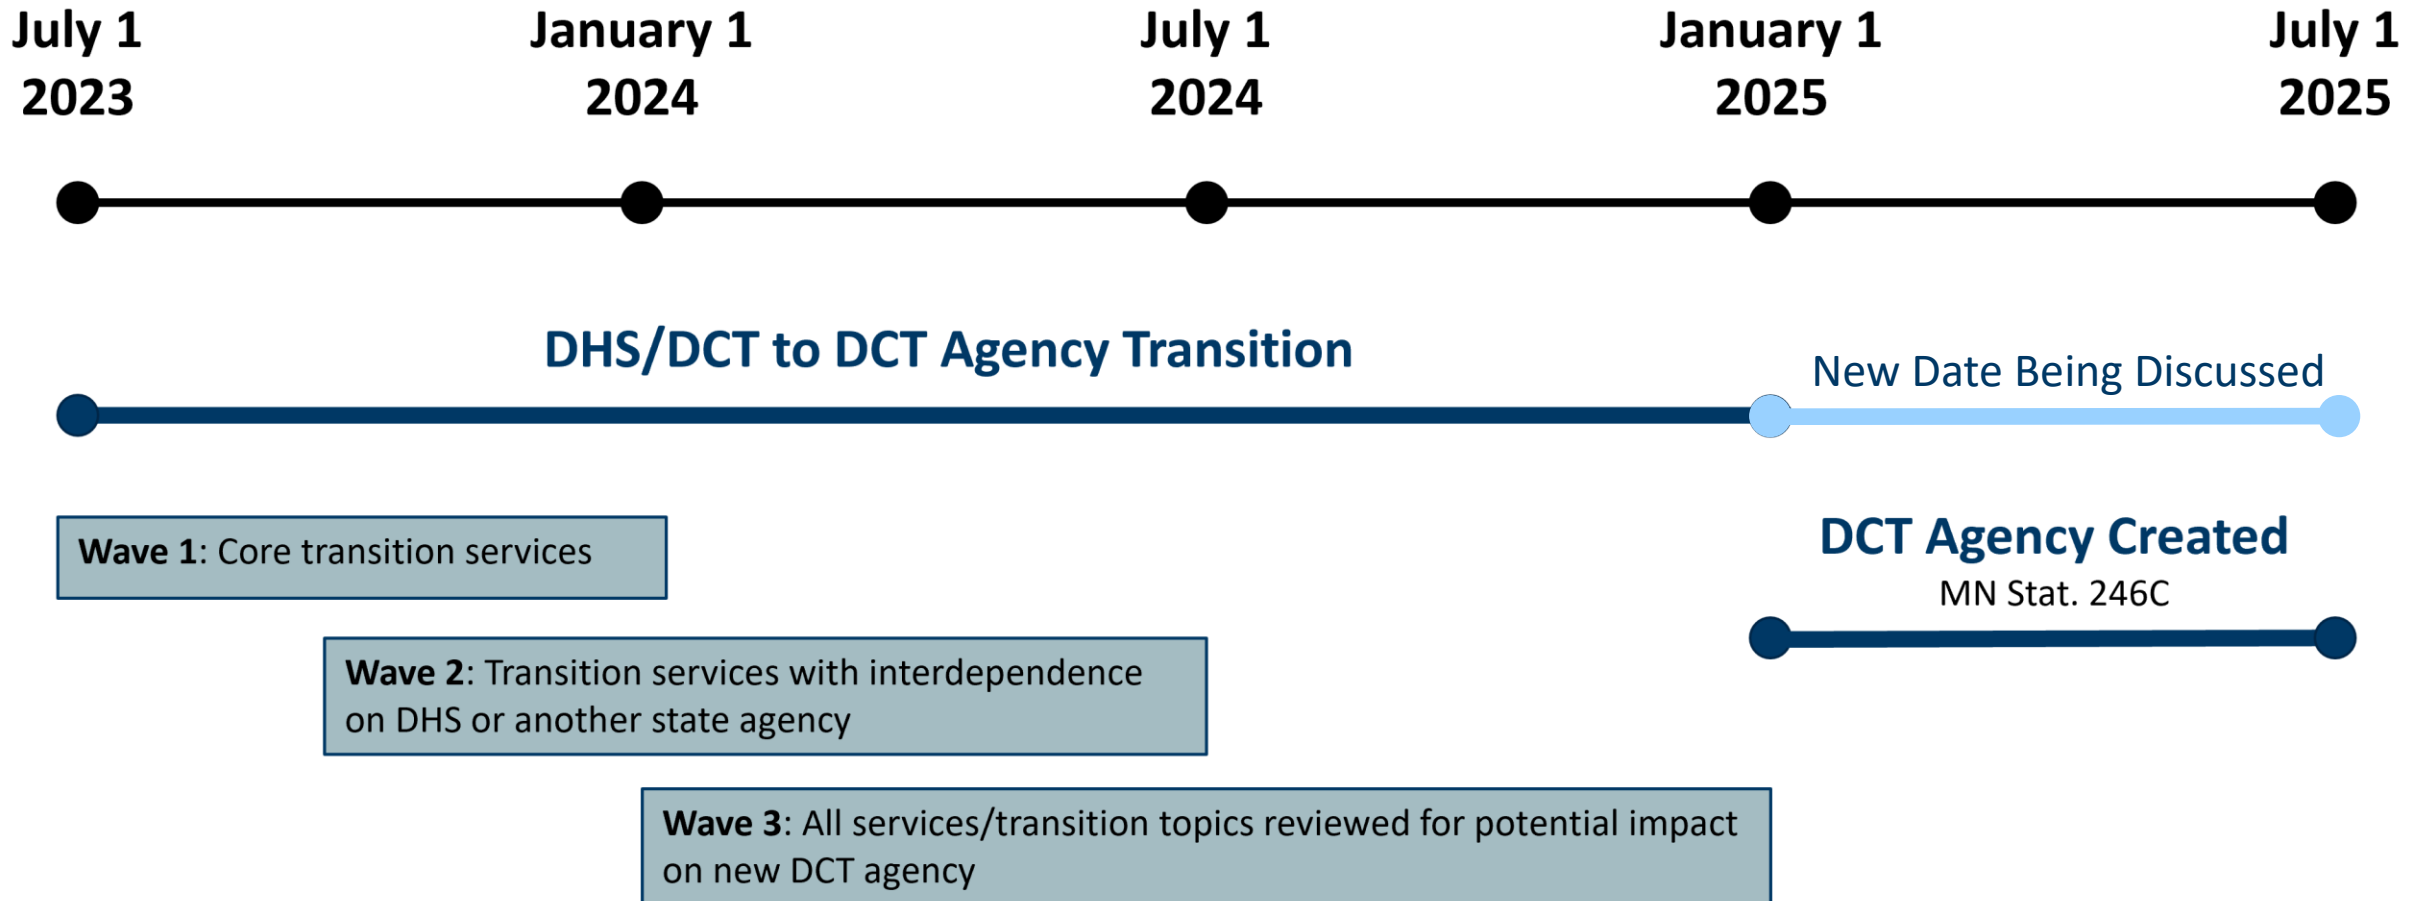

DCT creation project status: Wave 1

Key

- White: Not started
- Green: On schedule
- Yellow: Issue
- Red: Large Issue
- Blue: Action Plan Finalized
- Black: Action Plan Completed

Workgroup	Leader	IC Team Leader	Project Manager Lead	Status
MNIT	Nathan	Dan	Bob	○
Legislature	Carrie	Dan	Joan	●
Legal	Dale	Nancy F.	Joan	●
Communications	Chris	Nancy F.	Bob	●
Fiscal	Lynn	Nancy F.	Bob	●
HR	Cindy	Dan	Joan	●
DCT Board	Jeshua	Dan	Joan	●
Policy	Mindy	Nancy F.	Bob	●
Technology	Nathan	Dan	Bob	●
DCT Creation Language	Carrie	Dan	Bob	●
Revisors Office Review	Carrie	Dan	Joan	●
Governance	Dan	Dan	Joan	●
DCT Org Structure	Marshall	Dan	Joan	●
Branding	Chris	Nancy F.	Bob	● 1

As of 10/27/23

DCT creation project status: Wave 2

Key

White: Not started

Green: On schedule

Yellow: Issue

Red: Large Issue

Blue: Action Plan Finalized

Black: Action Plan Completed

Workgroup	Leader	LOG Team Leader	Project Manager Lead	Status
A - DHS/DCT Commissioner Responsibilities	Dan	Dan	Joan	○
A - Dept. Administration	Nancy F.	Nancy F.	Bob	●
A - MMB Activities	Lynn	Lynn	Joan	●
A - DHS/DCT Business Continuity	Joel	Nancy F.	Joan	●
A - DHS/DCT Regulatory	Terra	Nancy F.	Joan	●
B - DHS/DCT Data Management	Nathan	Dan	Bob	●
B - DHS/DCT Rule Making	Dale/Jeshua	Nancy F.	Bob	●
B - DHS/DCT Labor Management	Cindy	Dan	Joan	●
B - DCT Corp Compliance Infrastructure	Jeshua	Nancy F.	Joan	●
B - DHS/DCT Learning & Development	Noreen/Stacy	Dan	Bob	●
<i>Continued on next slide</i>				

As of 10/27/23

DCT creation project status: Wave 2

Key

White: Not started

Green: On schedule

Yellow: Issue

Red: Large Issue

Blue: Action Plan Finalized

Black: Action Plan Completed

Workgroup	Leader	LOG Team Leader	Project Manager Lead	Status
C - DHS/DCT Data Privacy	Dale/Jeshua	Dan	Bob	●
C - DHS/DCT Asset Management	Nancy F.	Nancy F.	Bob	●
C - Attorney General's Office	Dale	Dan	Joan	●
C - DHS/DCT Contracting/Procurement	Jeshua	Lynn	Bob	●
C - DHS/DCT Facilities Management	Nancy F.	Nancy F.	Bob	●
D - DHS/DCT Equity, Diversity & Culture	Stacy	Nancy F.	Joan	●
D - DHS/DCT Internal Audits	Jeshua	Lynn	Joan	●
D - DHS/DCT EOAD	Stacy	Cindy	Joan	●
D - DHS/DCT Emergency Mgt/BIA/COOPs	Joel	Nancy F.	Bob	●
D – Admissions and Clinical	Dr. Stevens	Dan	Bob	●
D – IRB/Data Analytics/Research	Doug L.	Dan	Bob	●

As of 10/27/23

DCT creation project status: Wave 3

Key

White: Not started

Green: On schedule

Yellow: Issue

Red: Large Issue

Blue: Action Plan Finalized

Black: Action Plan Completed

Workgroup	Leader	LOG Team Leader	Project Manager Lead	Status
Committee Structure	Nancy J/Terra	Nancy F.	Joan	●
Continuous Improvement	Terra	Dan	Joan	●
Core Divisions	Dan	Dan	Joan	●
HIMS	Sondra	Nancy F.	Bob	○
Medical Services	Dr. Stevens	Dan	Bob	●
Mission, Vision, Goals	Lisa/Chris	Dan	Bob	○
Pharmacy	Melissa	Dan	Bob	○
Quality	Terra	Nancy F.	Joan	●
Tribe/County/Other Relations	Carrie	Dan	Joan	●
Strategic Planning	Lisa DeJoras	Nancy F.	Joan	●
Support Services	Nancy	Nancy F.	Bob	○

As of 10/27/23

Key progress updates

- DCT has contracted with the Minnesota Hospital Association to consult on development of DCT board language and other health care issues. First draft is near completion.
- DCT has completed three listening sessions with unions, counties, and other stakeholders with good participation, feedback and proposed suggestions.
- DCT has begun dialog with tribes and has an additional meeting set on 11/16/23.
- The majority of DCT's 46 workgroups have begun meeting. One workgroup has completed action items. Eight workgroups have approved task lists, which are being worked on and included in the overall project planning.

Questions?

